

TMO/24/520/33

28-6-88



FELLESTRAADET FOR DET SOERLIGE AFRIKA
c/o NORWEGIAN PEOPLE'S AID
P.O. BOX 3381
DAR ES SALAAM

ATT: MR. K. MEKKI

Main Office:
Plogveien 1A
P.O. Box 97 - Manglerud
0612 Oslo 6
Tel. (temporary): (02) 67 70 90
and 67 70 57
International call: +47 2 67 70 90
or +47 2 67 70 57
Telex: 19361 Nplan N
Telefax: 68 80 89

Your ref.:

Our ref.: T024/NT217/88/CWG/jm DSM.1988.06.28

RE: T024. SUPERVISION OF ANC HOUSE AT KURASINI PLOT 28

Report on site visits 21/6 & 23/6/88.

21/6/88

1. In new building blockwork in progress, and curing being done. Most blockwork has reached bottom of beam or lintel level.
2. In building 1 window frames are being put in position with out hold fasts on. Frames should also be primed before being fixed.
3. Block making in progress.

Comments


Architectural drawings show some confusion between ring beam top height and false ceiling bottom height. Confusion must be sorted out before ring beam is cast.

23/6/88

1. Raining on site.
2. All walls in new building are up to beam bottom or lintel level.
3. In old unit one, false ceiling branderling in verandha in progress.
4. Priming of door & window frames for unit 1 in progress.
5. Generally, cleaning up of unit two being carried out.
6. Roof tiles not on site yet.

Cont'd ..2/..

Yours faithfully,
for NORPLAN A/S(T) BRANCH

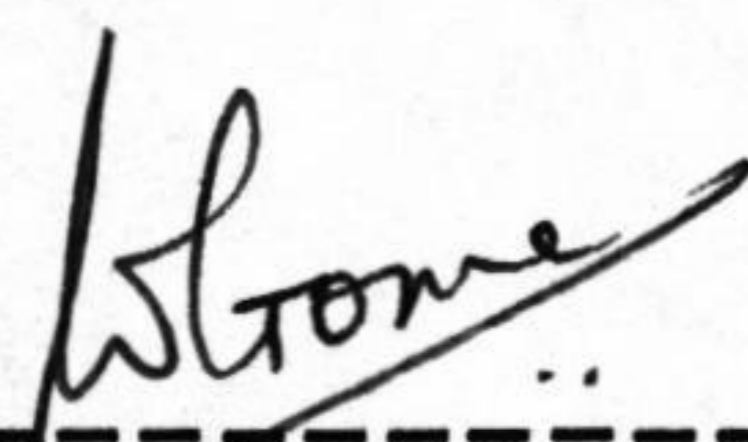

C.W.GOMES
PROJECTS ENGINEER

**NORPLAN
TANZANIA BRANCH
P.O. BOX 2820
DAR ES SALAAM
TANZANIA**

c.c Mr.K.Ekeberg , NORPLAN Oslo.
